
STATE: Michigan
GRANT TITLE: Iron Belle Trail Grants Round 2
REPORT TYPE: Progress Report
REPORTING PERIOD: Second Period Report



General Instructions

The GRANTEE must complete and submit a progress report of activities and accomplishments each quarter of the project period as well as a final report. The progress report will consist of the following:

1. Progress Report Narrative File Name written as:
Grant Number_Report Type_Reporting Period (ex. IBT16-18_Progress_12-31-16),
2. 5-10 photos of grant activities, or map/engineer drafts (if applicable)

The report narrative should follow the outline and guidance below.

Verification of activities is also requested in the form of photos, permits, outreach materials, survey, etc.

Summary

Provide a brief summary of your progress and accomplishments during the reporting period. This summary will be used for updating department staff, legislators, and the media, and it may be posted to the DNR website.

Oscoda Charter Township is studying/planning the Phase II portion of the Iron Belle Route that's located in Oscoda Township. This portion of the path will extend from the Oscoda Area High School west to Old Orchard Campground. This phase of the project involves developing a map or plan indicating the specific location of the path and determining opportunities for funding.

Discussion of Accomplishments

1. Describe the tasks completed and the progress made towards the goals of the grant, relative to the proposed timeline. Discussion should focus on the significant outcomes, milestones, and success stories of the project.

The following tasks have been completed as they relate to progress made towards the goals of the grant:

- Held a second project meeting on Wednesday, November 9th, 2016 with various project stakeholders including Oscoda Township staff, Consumers Energy, and IET representatives.
- Drove the route.
- Walked the route. (Photos attached)
- Identified all parcel land owners.
- Contacted the State of Michigan.
- Contacted the U.S. Forest Service.
- Coordination with Consumers Energy and addressed/resolved issues concerning transmission ROW.
- Identified the preferred route option and alternate route option. (Map attached)

2. Discuss any problems encountered during the reporting period that may interfere with meeting program/project objectives.

None.

3. List the proposed remedies of the problem(s) indicated in item 2.
4. Discuss whether or not the rate of expenditure with project goals during the reporting period and any budgetary issues the project may be experiencing. If the grantee is in need of an extension please write that here as well as in an official e-mail to the grant administrator.

Discussion of Future Activities

Provide a brief summary of planned activities to be completed within the next reporting period. Include how these activities will continue to make progress towards achieving the grant objectives.

The following planned activities are to be started/completed within the next reporting period:

- Complete cost estimate for construction.
- Develop typical path cross sections.
- Present draft preferred route option to Oscoda Township.

Progress Report Checklist

Review the following checklist of required documents for the grant program, noting which files need to be submitted with the progress report.

Required Documents	Submit
Progress Narrative	X
5-10 Publishable Photos	X
Outreach materials, including press releases, maps, or web links, etc.	X
Meeting, Training, or Event sign-in sheets	
Permits	
Survey records	

Please provide attachments in .pdf, .doc or .xls format

GRANTEE Statements

Statement	Signature of GRANTEE	Date
All required documents attached or located in project file		



Proposed location / north side of River Road.



Staked location.



Storm drain along route.



Path to be located in right-of-way here.




Route through woods.



Route behind store.






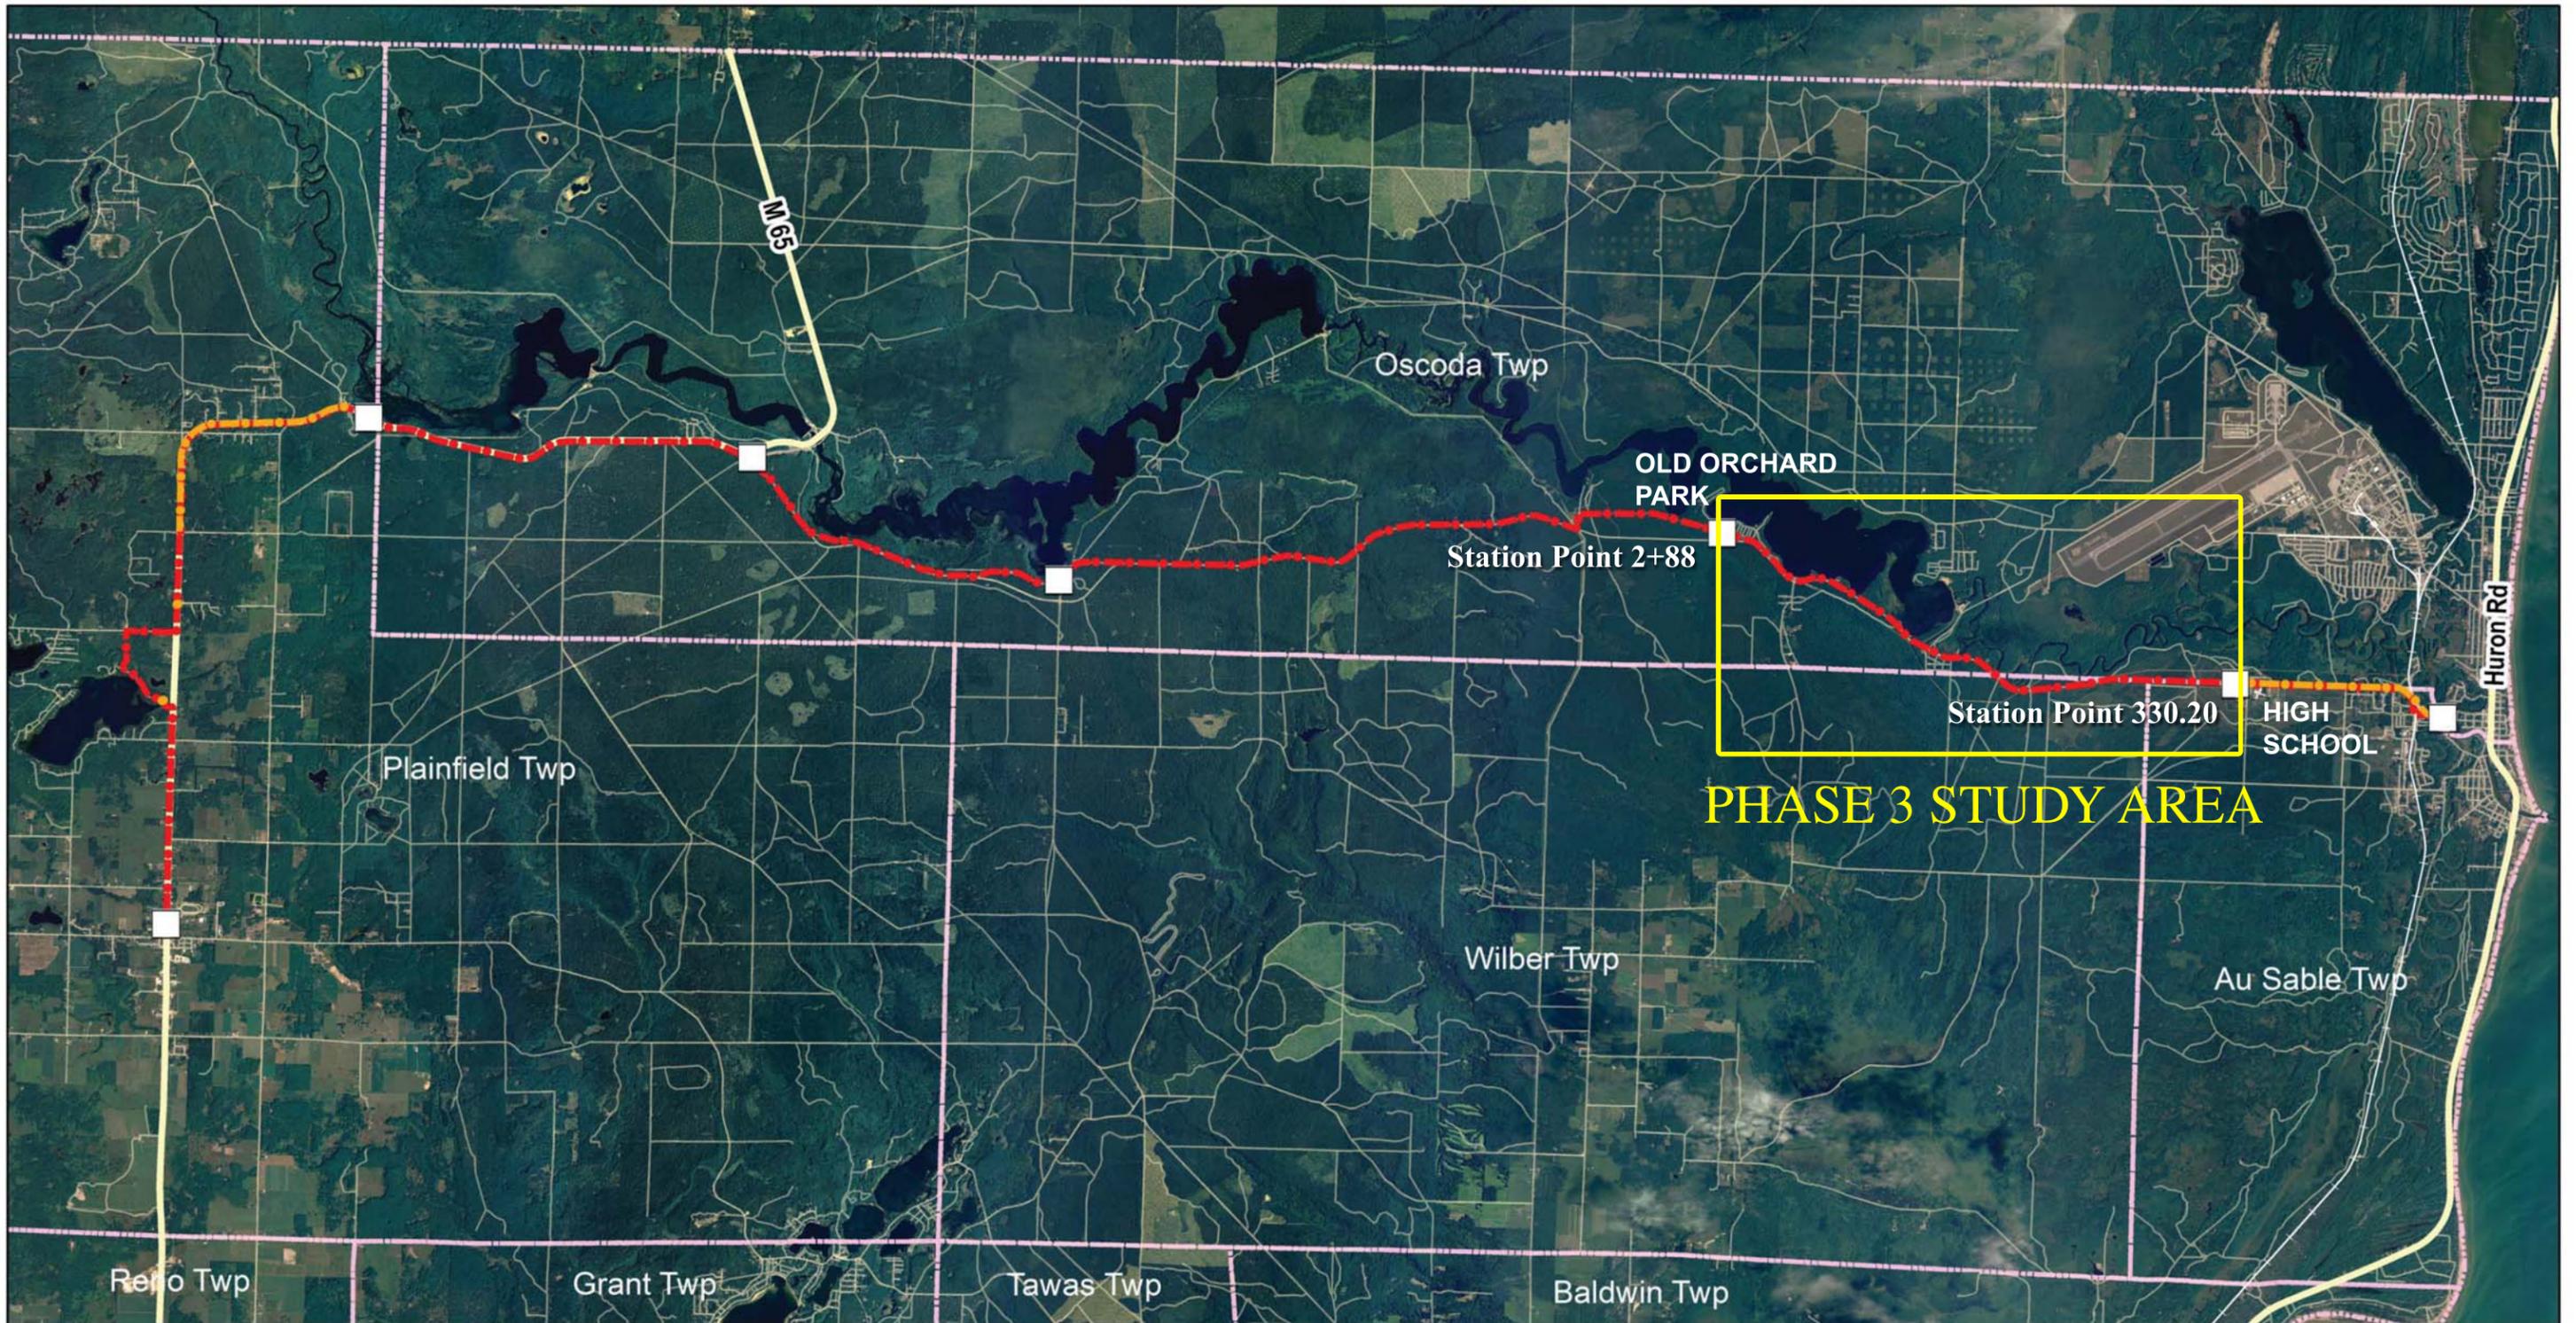

- Proposed Alt. Non-Motorized Path Section
- Proposed Non-Motorized Path
- Township Boundary
- Segment Break Points

Phase 3 - Old Orchard Park to High School Iosco County Non-Motorized Path



**PRELIMINARY ESTIMATE OF COST
MULTI-USE PATH
OSCODA & WILBER TOWNSHIP
IOSCO COUNTY, MICHIGAN**

WEST OF OLD ORCHARD CAMPGROUND TO OSCODA SCHOOLS

Item No.	Estimated Quantity	Unit	Description	Unit Price	Amount
1.	1	LSUM	Mobilization, Max. _____	\$151,000.00	\$151,000.00
2.	2.0	Acre	Clearing	\$8,000.00	\$16,000.00
3.	105	Ft	Erosion Control, Check Dam, Stone	\$20.00	\$2,100.00
4.	7	Ea	Erosion Control, Sediment Trap	\$150.00	\$1,050.00
5.	4550	Ft	Erosion Control, Silt Fence	\$2.00	\$9,100.00
6.	300	Syd	Approach, CI II, 6 inch	\$10.00	\$3,000.00
7.	10	Ea	Culv End Sect, 12 inch	\$325.00	\$3,250.00
8.	120	Ft	Culv, CI A, 12 inch	\$50.00	\$6,000.00
9.	80	Ft	Detectable Warning Surface	\$40.00	\$3,200.00
10.	400	Sft	Sidewalk Ramp, Conc, 6 inch	\$7.00	\$2,800.00
11.	32602	Ft	Shared Use Path, Grading	\$7.70	\$251,035.40
12.	4700	Ton	Shared Use Path, HMA	\$90.00	\$423,000.00
13.	40000	Syd	Shared Use Path, Aggregate, 6 inch	\$7.50	\$300,000.00
14.	300	Ft	Fence, Chain Link, 60 inch	\$25.00	\$7,500.00
15.	44	Ea	Permanent Traffic Signs	\$150.00	\$6,600.00
16.	1500	Ft	Pavt Mrkg, Ovly Cold Plastic, 6 inch, Crosswall	\$2.75	\$4,125.00
17.	1	LSUM	Maintaining Traffic	\$30,000.00	\$30,000.00
18.	300	Syd	Riprap, Plain	\$60.00	\$18,000.00
19.	360000	Sft	Non Selective Weed Spray Under Asphal	\$0.05	\$18,000.00
20.	43500	Syd	Slope Restoration	\$2.50	\$108,750.00
21.	1	LSUM	Trail Amenities (Interpretive signs, benches, etc)	\$30,000.00	\$30,000.00
22.	3	Ea	Nature Overlook	\$50,000.00	\$150,000.00
Contingencies					<u>\$154,489.60</u>
Construction Subtotal					\$1,699,000.00
Design Survey					\$40,000.00
Design Engineering					\$119,000.00
Construction Administration, Staking, Inspection, & Material Testin					<u>\$204,000.00</u>
TOTAL PRELIMINARY ESTIMATE OF COST					\$2,062,000.00
